

Date Range: June 8, 2025 through June 14, 2025 Perimeter Air Monitoring Station Summary Volatile Organic Compounds (VOCs), PM10 (Dust), Wind Direction

Dust (PM-10) Project Action Level – 150 μg/m³ VOC Project Action Level – 5 ppm


Station 1- AQS1 10072023-2370 (Blue) North Perimeter

Station 2- AQS1 10072023-2371 (Red) East Perimeter

Station 3- AQS1 23092021-1781 (Green) South Perimeter


Station 4- DS 11122020-1470A (Yellow) West Perimeter

VOCs

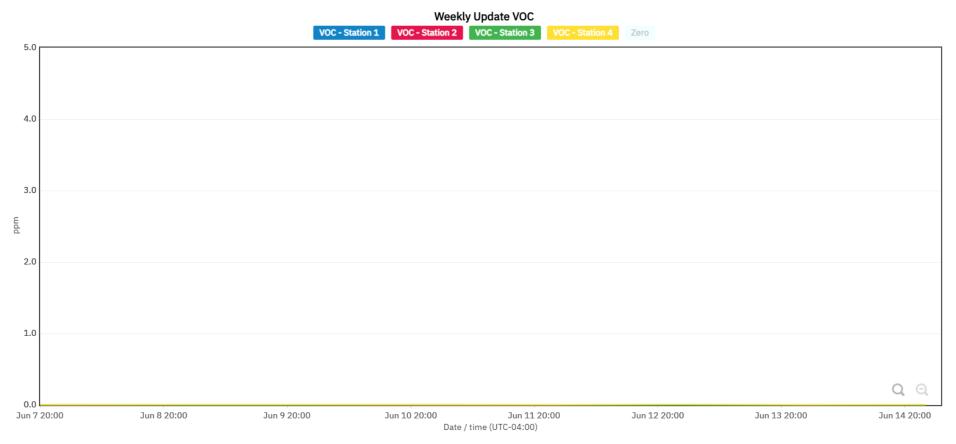




Dust (PM10)

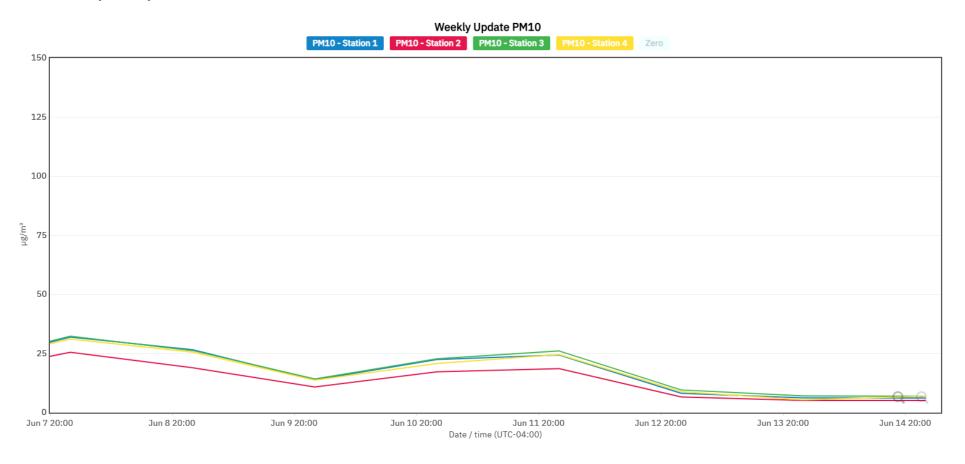



Wind Rose

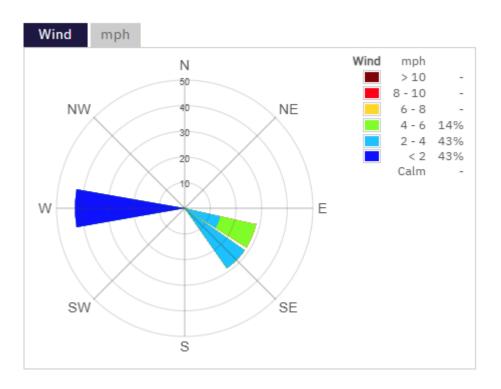

Notes:

- 1. Weekly VOC calibration was on 06/13/2025.
- 2. Air quality alerts due to Canadian wildfire smoke were in effect during the week of June 8th.
- 3. On site work commences at approximately 7:30 am and stops at approximately 17:30 daily.
- 4. Contractor working days during the week of 06/08/2025 were Monday through Saturday.
- 5. Short-Term Response Levels at the fence line are: Dust 150 ug/m³ for 15 minutes and Total VOCs 0.5 ppm for 15 minutes.
- 6. Directions shown on Wind Rose are the direction the wind is blowing from.



