Progress Schedule_12-10-19.mpp

ID	Task Name	Duration	Start	Finish
1	**Mobilization an Setup**	**12 days**	**Thu 9/19/19**	**Fri 10/4/19**
2	Notice To Proceed	1 day	Thu 9/19/19	Thu 9/19/19
3	Pre Construction Submittal & Meeting	5 days	Fri 9/20/19	Thu 9/26/19
4	Mobilize & Setup Facilities	5 days	Mon 9/30/19	Fri 10/4/19
5	**North Rum Creek**	**95.26 days**	**Wed 10/2/19**	**Tue 2/25/20**
6	Close White Pine Trail	0 days	Wed 10/2/19	Wed 10/2/19
7	Remove & Install Temporary Fence	4 days	Tue 10/8/19	Fri 10/11/19
8	Install Sediment & Erosion Control	3 days	Thu 10/3/19	Mon 10/7/19
9	Temporary Access Road	4 days	Mon 10/7/19	Thu 10/10/19
10	Clear & Grub River Bank	5 days	Tue 10/8/19	Mon 10/14/19
11	Install Cofferdam N1 & N2	14 days	Fri 11/8/19	Tue 1/7/20
12	Dewater Area N1 & N2	17.63 days	Mon 11/11/19	Fri 1/31/20
13	Excavate Area N1	23 days	Tue 11/12/19	Tue 1/14/20
14	Excavate Area N2B	1 day	Tue 12/10/19	Wed 1/15/20
15	Excavate Area N2A	10 days	Wed 1/15/20	Wed 1/29/20
16	Transport Impacted Material	32 days	Wed 11/13/19	Wed 1/8/20
17	RIP RAP Bank Protection	13 days	Wed 1/29/20	Mon 2/17/20
18	Backfill Excavations	13 days	Wed 1/29/20	Mon 2/17/20
19	Remove Cofferdam	2 days	Mon 2/17/20	Wed 2/19/20
20	Place Topsoil	2 days	Mon 2/17/20	Wed 2/19/20
21	Install Erosion Control Blanket	2 days	Wed 2/19/20	Fri 2/21/20
22	White Pine Trail Subbase	4 days	Wed 2/19/20	Tue 2/25/20
23	**South Rum Creek**	**97.26 days**	**Mon 10/7/19**	**Tue 3/3/20**
24	Remove & Install Temporary Fence	4 days	Mon 10/7/19	Thu 10/10/19
25	Install Sediment & Erosion Control	1 day	Fri 10/11/19	Fri 10/11/19
26	Temporary Access Road	1.95 days	Fri 10/11/19	Mon 10/14/19
27	Clear & Grub Areas S2, S4, S5, S6	2 days	Thu 10/10/19	Fri 10/11/19
28	Excavate Area S1	36 days	Tue 10/22/19	Wed 12/18/19
29	Transport Impacted Material S1	40 days	Tue 10/22/19	Wed 12/18/19
30	Backfill Area S1	1 day	Wed 10/23/19	Thu 12/19/19
31	**Excavation of S7**	**43 days**	**Mon 10/28/19**	**Tue 1/7/20**
32	Fence Removal & Install Erosion Controls S7	2 days	Mon 10/28/19	Tue 10/29/19
33	Install Bladderdam Cofferdam S7	1 day	Wed 10/30/19	Wed 10/30/19
34	Install Sheetpile Cofferdam S7	4 days	Tue 11/5/19	Fri 11/8/19
35	Dewater Area S7	1 day	Fri 11/8/19	Fri 11/8/19
36	Excavate Area S7	21 days	Thu 10/31/19	Wed 12/11/19
37	Dewater Area S7	7 days	Mon 12/16/19	Thu 1/2/20
38	Install Geogrid and Fabric	3 days	Mon 12/16/19	Wed 12/18/19
39	Backfill Area S7	4 days	Thu 12/19/19	Thu 1/2/20
40	Place Rip Rap S7	2 days	Fri 1/3/20	Mon 1/6/20
41	Restoration S7	1 day	Tue 1/7/20	Tue 1/7/20
42	Install Cofferdam Area S2	0 days	Wed 10/16/19	Wed 10/16/19
43	Dewater Area S2	1 day	Fri 10/18/19	Fri 10/18/19
44	Excavate Area S2	2 days	Fri 10/18/19	Mon 10/21/19
45	Sample and Re-excavate Area S2	15 days	Tue 10/22/19	Mon 11/11/19
46	Backfill S2	20 days	Tue 10/29/19	Mon 11/25/19
47	Dewater Areas S3, S4, S6	29 days	Mon 10/21/19	Mon 12/2/19
48	Transport Impacted Material S3, S4, S6	37 days	Tue 10/22/19	Fri 12/13/19
49	Excavate Area S3	2 days	Mon 10/21/19	Tue 10/22/19
50	Sample and Re-excavate Area S3	16 days	Wed 10/23/19	Wed 11/13/19
51	Backfill Area S3	3 days	Thu 11/14/19	Mon 11/18/19
52	Install Cofferdam Areas S4	2 days	Sat 10/19/19	Tue 10/22/19
53	Excavate S4	6 days	Mon 10/21/19	Mon 10/28/19
54	Sample and Re-excavate Area S4	18 days	Tue 11/5/19	Mon 12/2/19
55	Install Cofferdam at S5	1 day	Wed 1/8/20	Wed 1/8/20
56	Dewater Area S5	1 day	Thu 1/9/20	Thu 1/9/20
57	Excavate S5	2 days	Fri 1/10/20	Mon 1/13/20
58	Install Cofferdam at S6	1 day	Thu 10/17/19	Thu 10/17/19
59	Dewater Area S6	1 day	Fri 10/18/19	Fri 10/18/19
60	Excavate S6	1 day	Fri 10/18/19	Fri 10/18/19
61	Place Topsoil	2 days	Tue 1/14/20	Wed 1/15/20
62	Install Erosion Control Blanket	2 days	Thu 1/16/20	Fri 1/17/20
63	White Pine Trail Subbase	2 days	Mon 1/20/20	Tue 1/21/20
64	Reopen White Pine Trail	0 days	Tue 2/25/20	Tue 2/25/20
65	Remove Access Road & Stage Material Onsite	3 days	Wed 2/19/20	Mon 2/24/20
66	Demob Equipment & Facilities	5 days	Tue 2/25/20	Tue 3/3/20

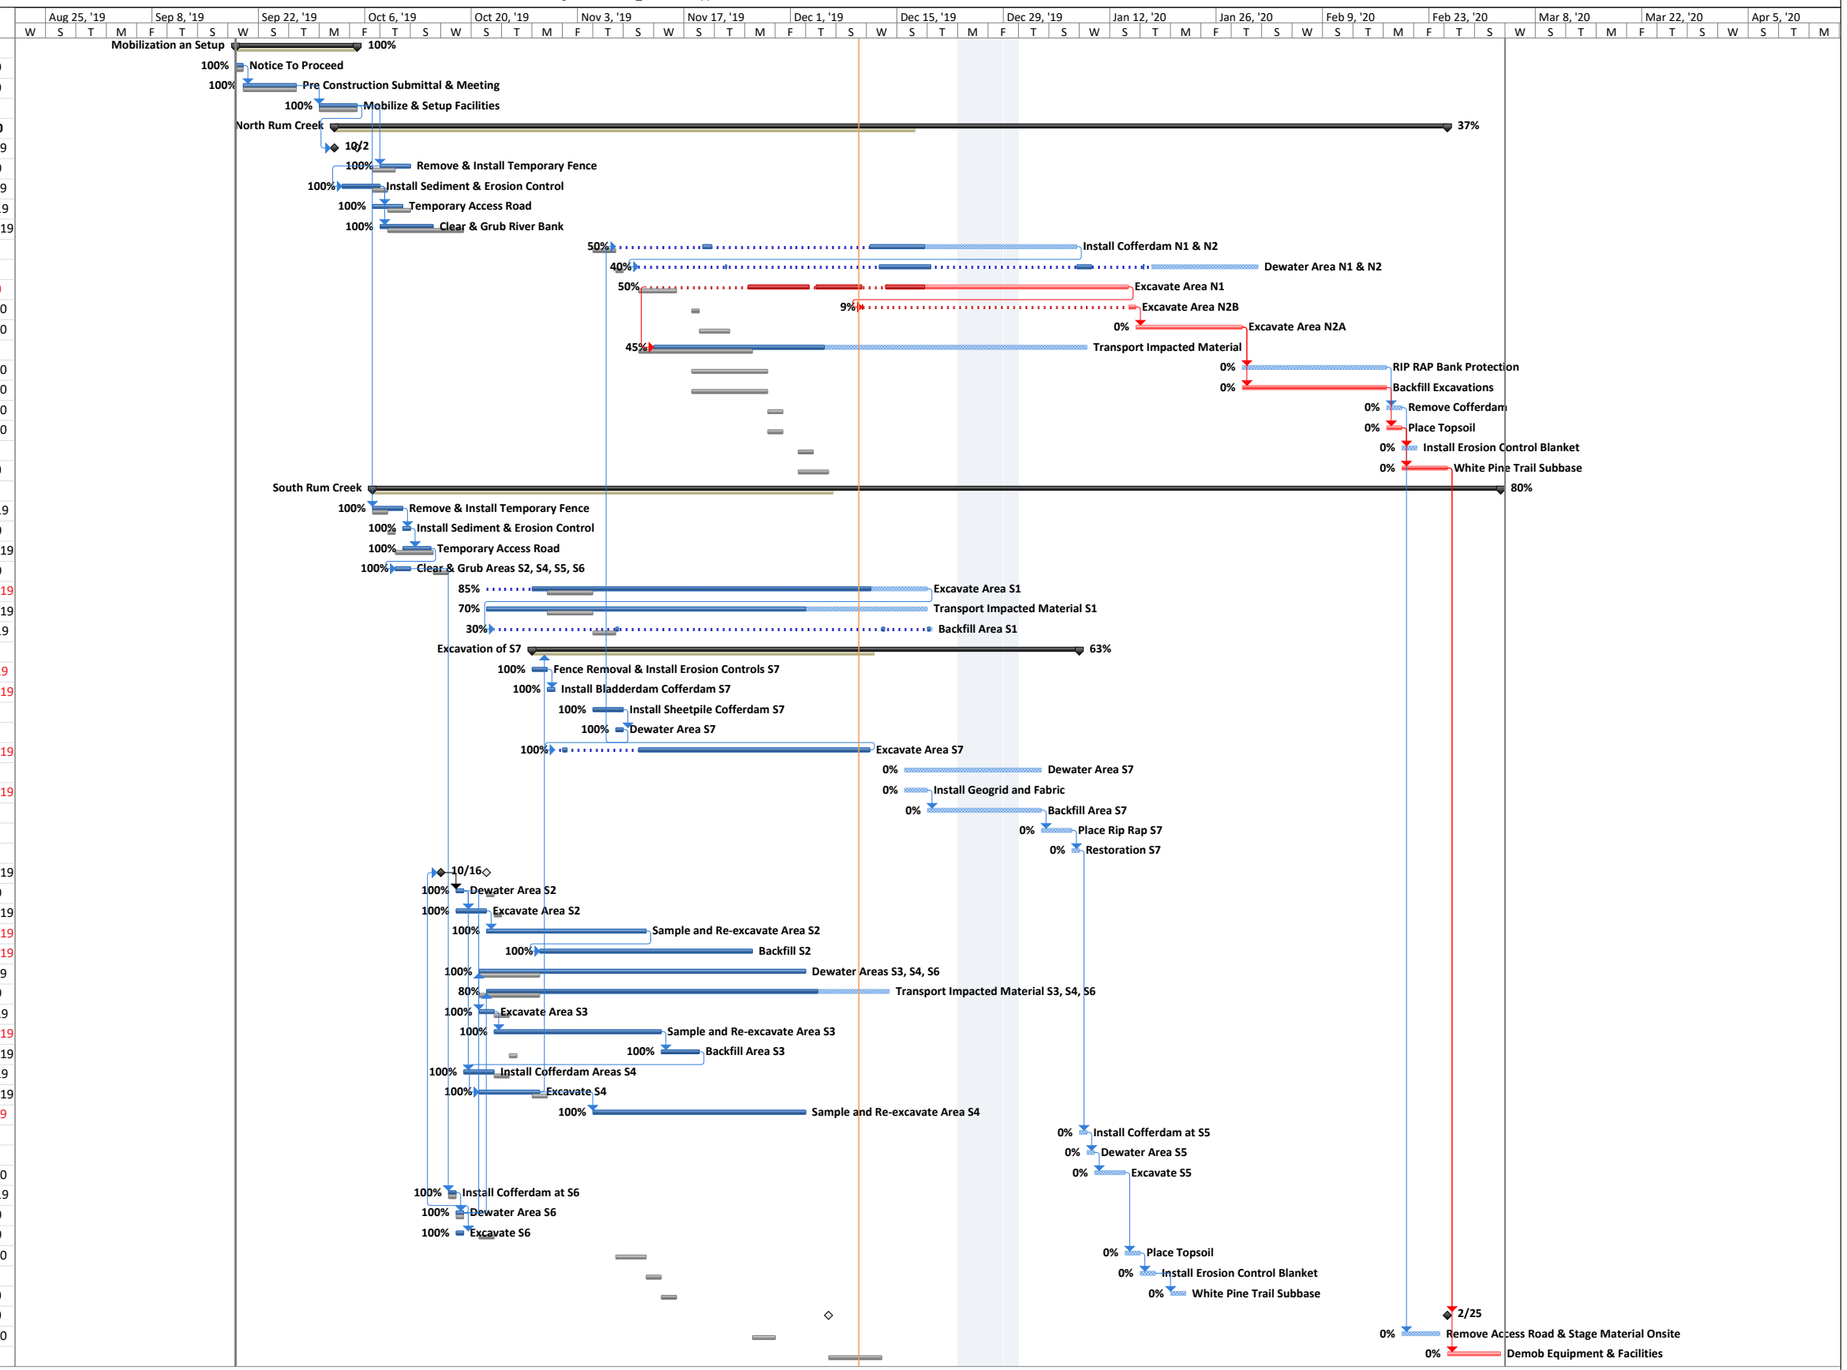

Critical | Critical Split | Critical Progress | Task | Split | Task Progress | Manual Task | Start-only | Finish-only | Duration-only | Baseline | Baseline Split | Baseline Milestone | Milestone | Summary Progress | Summary | Manual Summary | Project Summary | External Tasks | External Milestone | Inactive Task | Inactive Milestone | Inactive Summary | Deadline
